


Sequoia H/R Mech. ASY 71907-0C020 & 30 & 50

ID	Task Name	Duration	% Complete	Start	Finish	Sep '06				Oct '06				Nov '06				Dec '06				Jan '07			
						8/13	8/20	8/27	9/3	9/10	9/17	9/24	10/1	10/8	10/15	10/22	10/29	11/5	11/12	11/19	11/26	12/3	12/10	12/17	12/24
20	✓ 1st Foam Mold- Pad Front-71953-XC00-A	22 days	100%	Fri 8/25/06	Mon 9/25/06	[Task Bar]																			
21	✓ 2-3 Foam Molds- Pad Front-71953-XC00-A	55 days	100%	Mon 9/25/06	Fri 12/8/06					[Task Bar]															
22	✓ 1st Foam Mold- Pad Rear-71953-XC01-A	22 days	100%	Fri 8/25/06	Mon 9/25/06	[Task Bar]																			
23	✓ 2-3 Foam Molds- Pad Rear-71953-XC01-A	55 days	100%	Mon 9/25/06	Fri 12/8/06					[Task Bar]															
24	✓ Vendor PPAP	50 days	100%	Mon 9/25/06	Fri 12/1/06					[Task Bar]															
25	✓ 71959-X7C00-C_Holder Marwood	50 days	100%	Mon 9/25/06	Fri 12/1/06					[Task Bar]															
26	✓ 71971-X7C00-B_Bracket Marwood	50 days	100%	Mon 9/25/06	Fri 12/1/06					[Task Bar]															
27	✓ 71972-X7C00-B_Bracket Marwood	50 days	100%	Mon 9/25/06	Fri 12/1/06					[Task Bar]															
28	✓ 71971-X7C01-A_Bracket Marwood	50 days	100%	Mon 9/25/06	Fri 12/1/06					[Task Bar]															
29	✓ 72989-X7C00-B_Plate Marwood	50 days	100%	Mon 9/25/06	Fri 12/1/06					[Task Bar]															
30	✓ 71945-X7C00-A_Plate GFM	50 days	100%	Mon 9/25/06	Fri 12/1/06					[Task Bar]															
31	✓ 71949-X7C00-A_Hook GFM	50 days	100%	Mon 9/25/06	Fri 12/1/06					[Task Bar]															
32	✓ 71983-X7C00-A_Guide GFM	50 days	100%	Mon 9/25/06	Fri 12/1/06					[Task Bar]															
33	✓ 74917-X7C00-A_Stopper GFM	50 days	100%	Mon 9/25/06	Fri 12/1/06					[Task Bar]															
34	✓ 71987-X7C000-A_Cable Hilex	47 days	100%	Mon 9/25/06	Tue 11/28/06					[Task Bar]															
35	✓ 71987-X7C001_Cable Hilex	47 days	100%	Mon 9/25/06	Tue 11/28/06					[Task Bar]															

3rd row Headrest Mechanism Lisa Bilbrey January 16, 2007	Task		Summary		Rolled Up Progress		Project Summary	
	Progress		Rolled Up Task		Split		Group By Summary	
	Milestone		Rolled Up Milestone		External Tasks		Deadline	

Sequoia H/R Mech. ASY 71907-0C020 & 30 & 50

Feb '07	Mar '07	Apr '07	May '07	Jun '07	Jul '07	Aug '07	Sep '07	Oct '07	Nov '07	Dec '07	Jan '08
2/4 2/11 2/18 2/25	3/4 3/11 3/18 3/25	4/1 4/8 4/15 4/22 4/29	5/6 5/13 5/20 5/27	6/3 6/10 6/17 6/24	7/1 7/8 7/15 7/22 7/29	8/5 8/12 8/19 8/26	9/2 9/9 9/16 9/23 9/30	10/7 10/14 10/21 10/28	11/4 11/11 11/18 11/25	12/2 12/9 12/16 12/23	1/6 1/13 1/20

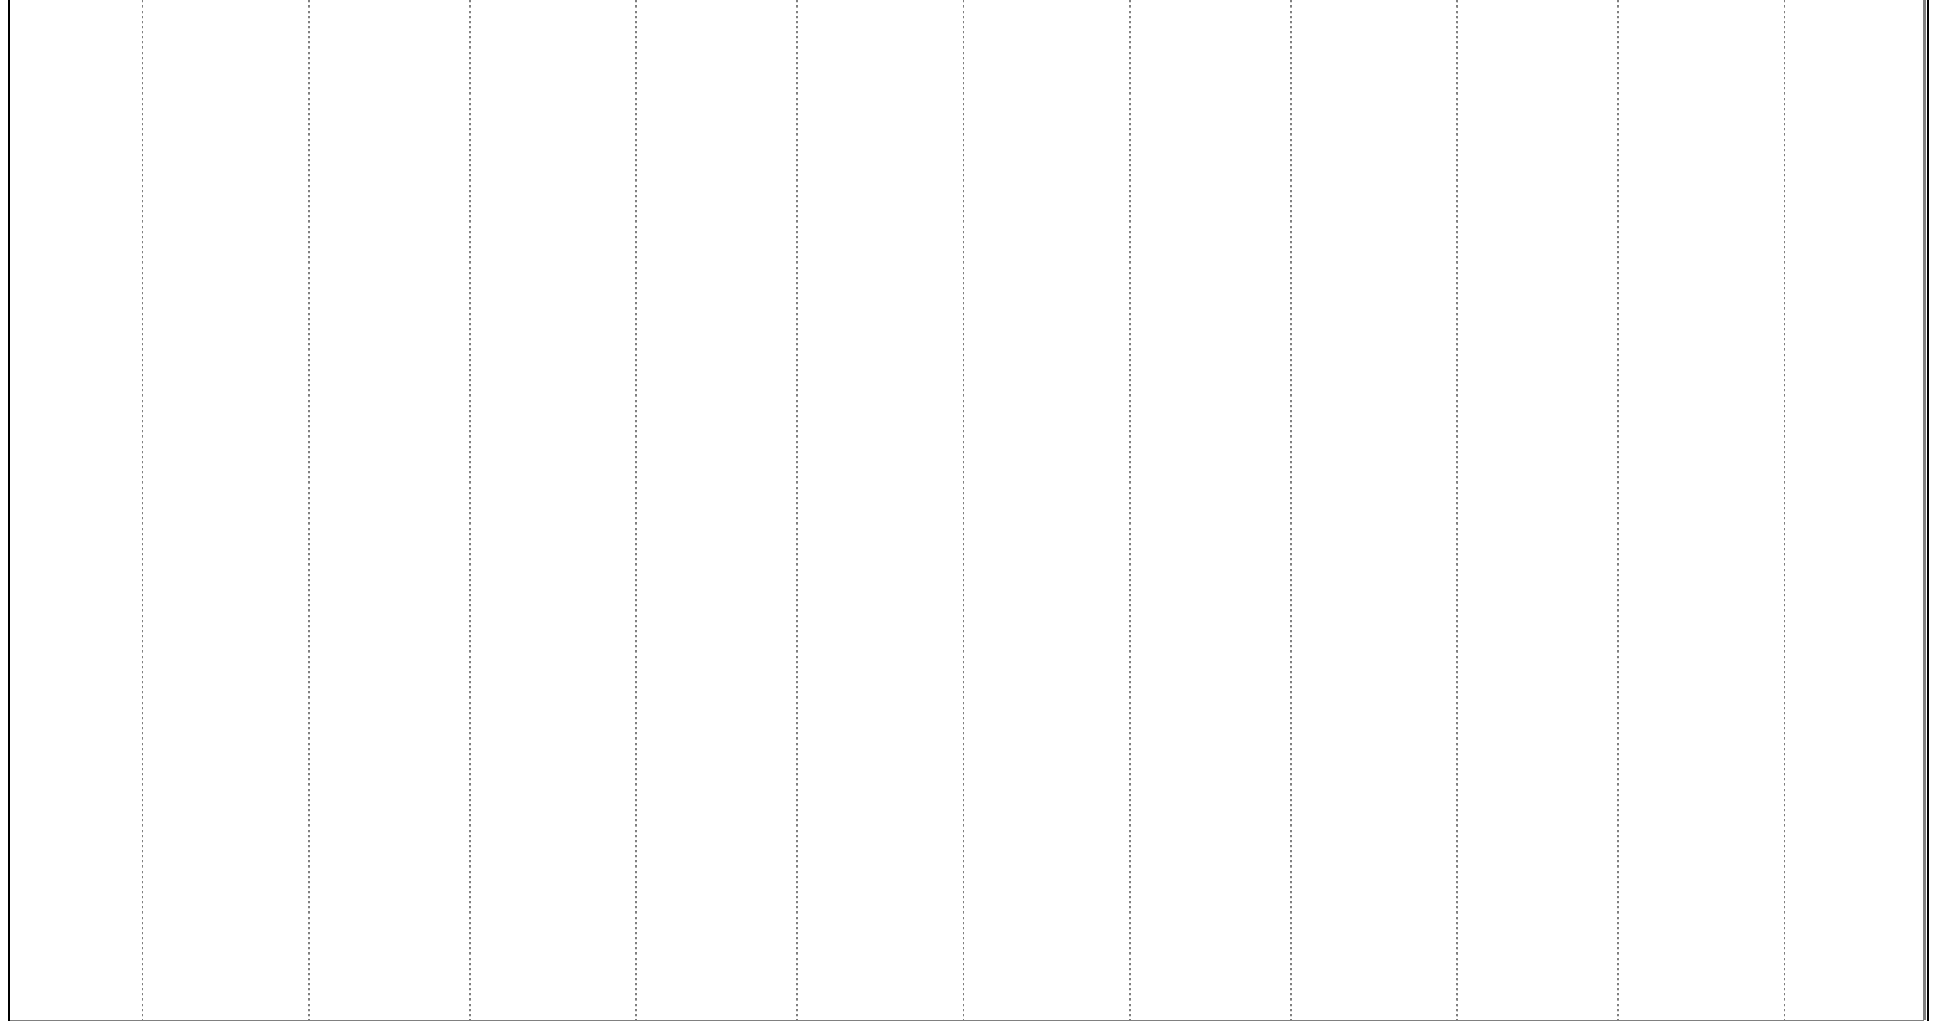


3rd row Headrest Mechanism
 Lisa Bilbrey
 January 16, 2007

Task		Summary		Rolled Up Progress		Project Summary	
Progress		Rolled Up Task		Split		Group By Summary	
Milestone		Rolled Up Milestone		External Tasks		Deadline	

Sequoia H/R Mech. ASY 71907-0C020 & 30 & 50

Feb '07	Mar '07	Apr '07	May '07	Jun '07	Jul '07	Aug '07	Sep '07	Oct '07	Nov '07	Dec '07	Jan '08
2/4 2/11 2/18 2/25	3/4 3/11 3/18 3/25	4/1 4/8 4/15 4/22 4/29	5/6 5/13 5/20 5/27	6/3 6/10 6/17 6/24	7/1 7/8 7/15 7/22 7/29	8/5 8/12 8/19 8/26	9/2 9/9 9/16 9/23 9/30	10/7 10/14 10/21 10/28	11/4 11/11 11/18 11/25	12/2 12/9 12/16 12/23	1/6 1/13 1/20

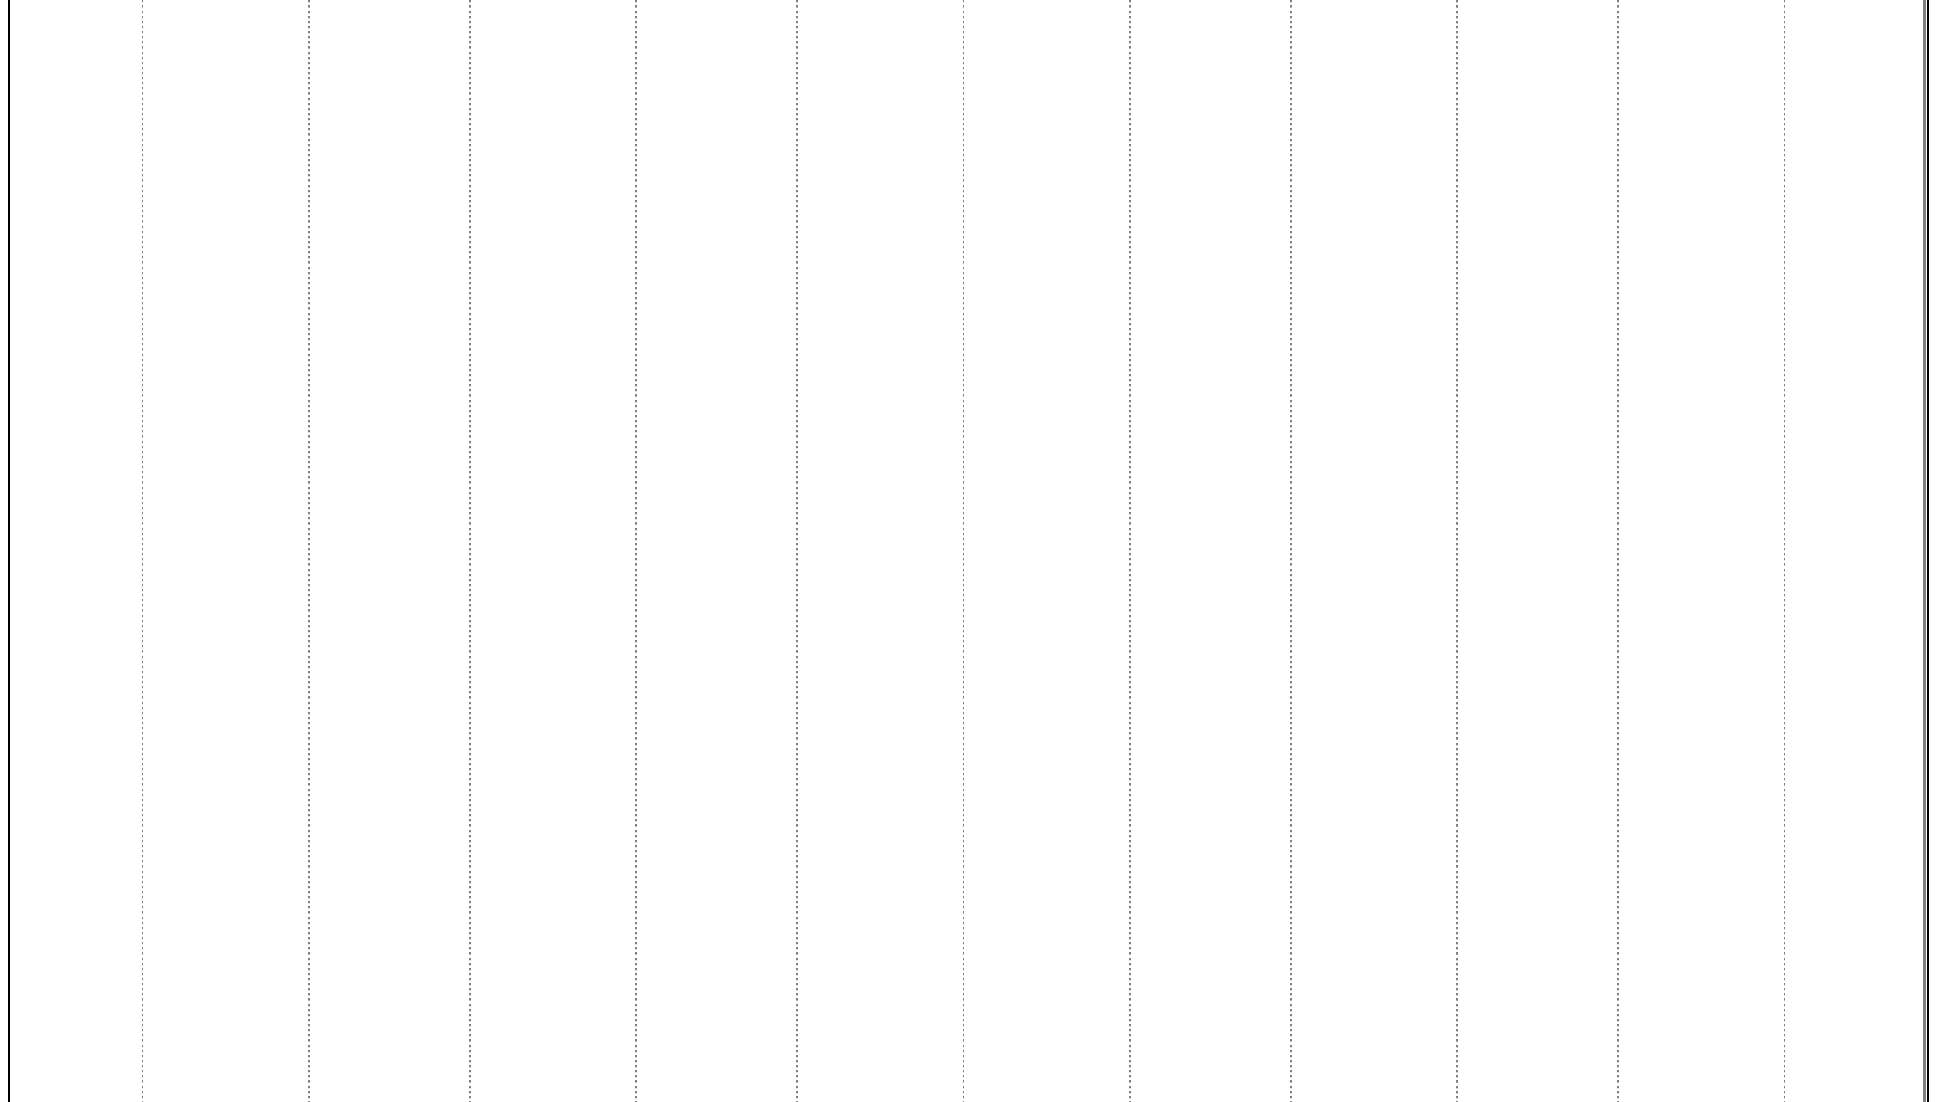

3rd row Headrest Mechanism
 Lisa Bilbrey
 January 16, 2007

Task		Summary		Rolled Up Progress		Project Summary	
Progress		Rolled Up Task		Split		Group By Summary	
Milestone		Rolled Up Milestone		External Tasks		Deadline	

Sequoia H/R Mech. ASY 71907-0C020 & 30 & 50

Feb '07	Mar '07	Apr '07	May '07	Jun '07	Jul '07	Aug '07	Sep '07	Oct '07	Nov '07	Dec '07	Jan '08
2/4 2/11 2/18 2/25	3/4 3/11 3/18 3/25	4/1 4/8 4/15 4/22 4/29	5/6 5/13 5/20 5/27	6/3 6/10 6/17 6/24	7/1 7/8 7/15 7/22 7/29	8/5 8/12 8/19 8/26	9/2 9/9 9/16 9/23 9/30	10/7 10/14 10/21 10/28	11/4 11/11 11/18 11/25	12/2 12/9 12/16 12/23	1/6 1/13 1/20




3rd row Headrest Mechanism
 Lisa Bilbrey
 January 16, 2007

Task		Summary		Rolled Up Progress		Project Summary	
Progress		Rolled Up Task		Split		Group By Summary	
Milestone		Rolled Up Milestone		External Tasks		Deadline	

Sequoia H/R Mech. ASY 71907-0C020 & 30 & 50


Feb '07	Mar '07	Apr '07	May '07	Jun '07	Jul '07	Aug '07	Sep '07	Oct '07	Nov '07	Dec '07	Jan '08
2/4 2/11 2/18 2/25	3/4 3/11 3/18 3/25	4/1 4/8 4/15 4/22 4/29	5/6 5/13 5/20 5/27	6/3 6/10 6/17 6/24	7/1 7/8 7/15 7/22 7/29	8/5 8/12 8/19 8/26	9/2 9/9 9/16 9/23 9/30	10/7 10/14 10/21 10/28	11/4 11/11 11/18 11/25	12/2 12/9 12/16 12/23	1/6 1/13 1/20

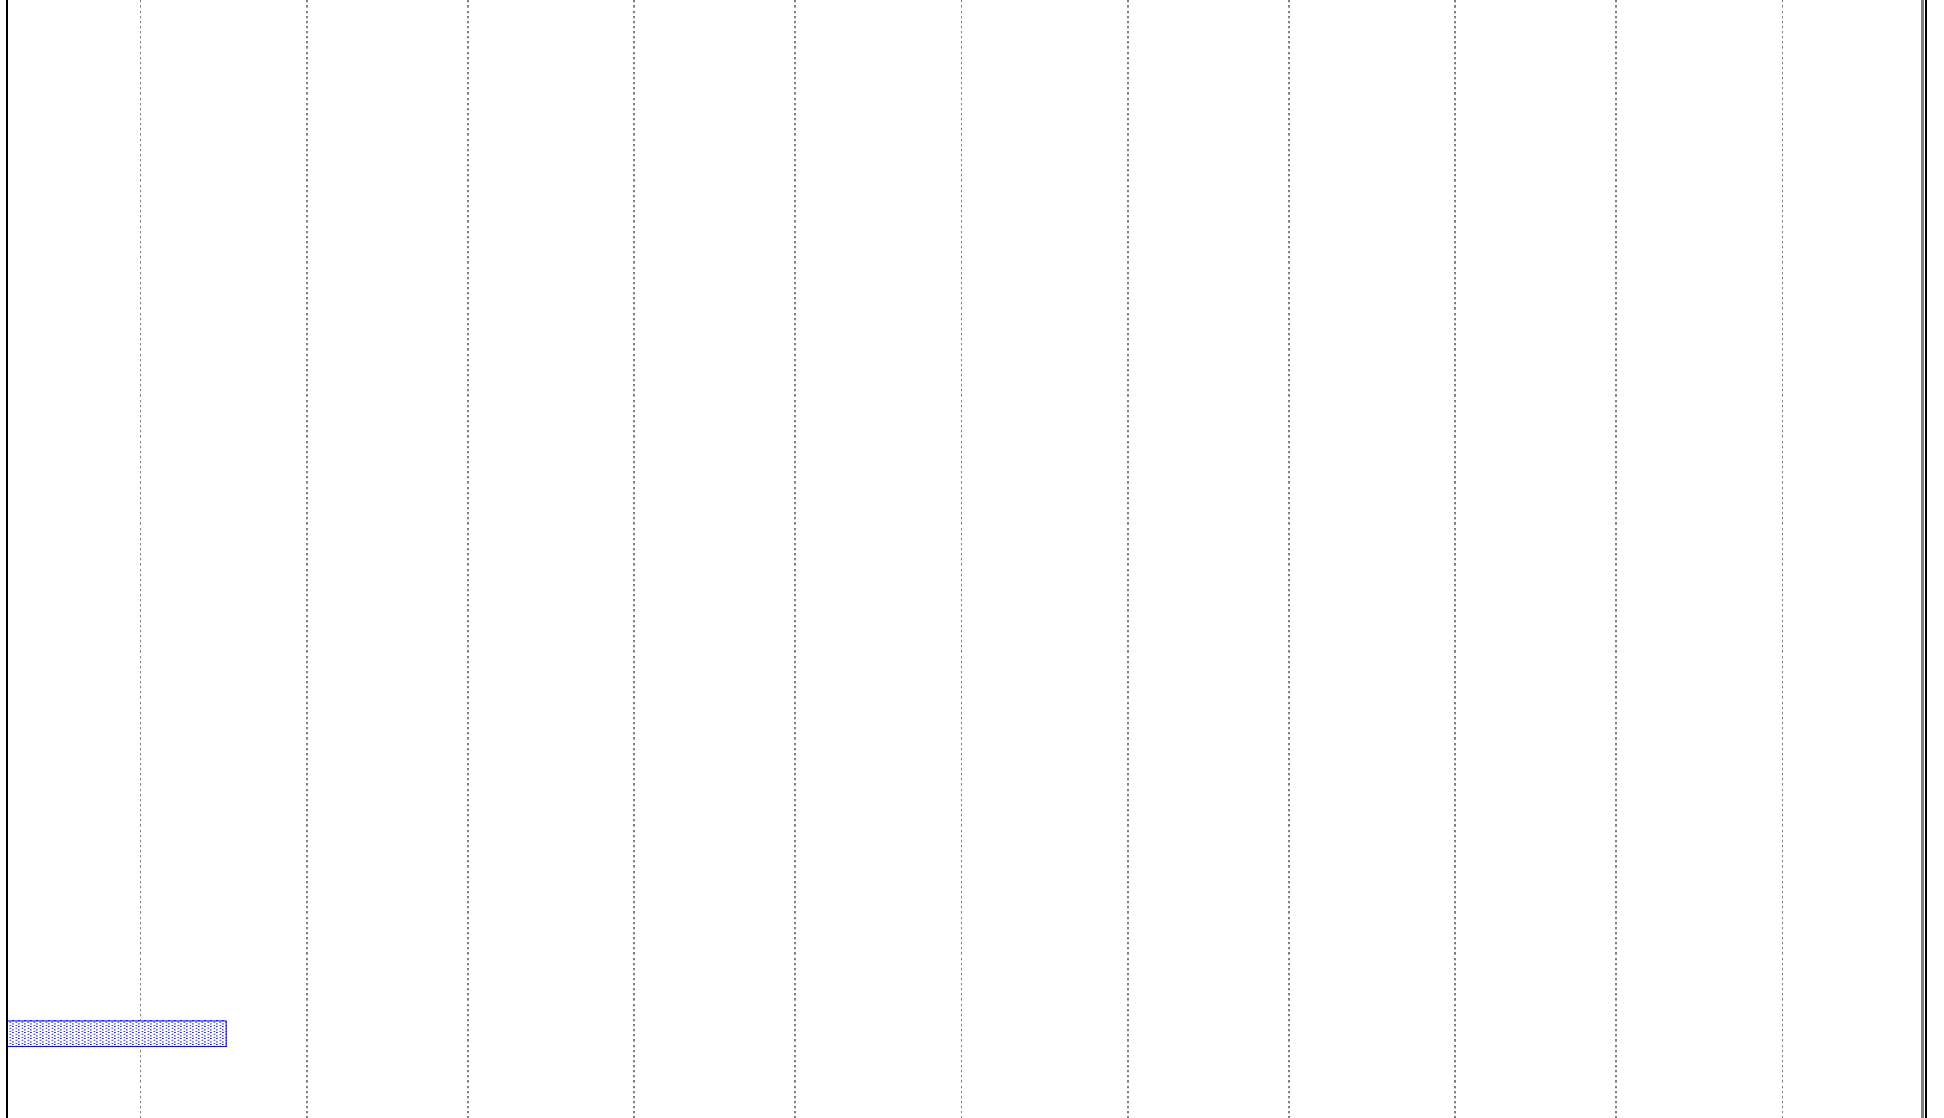









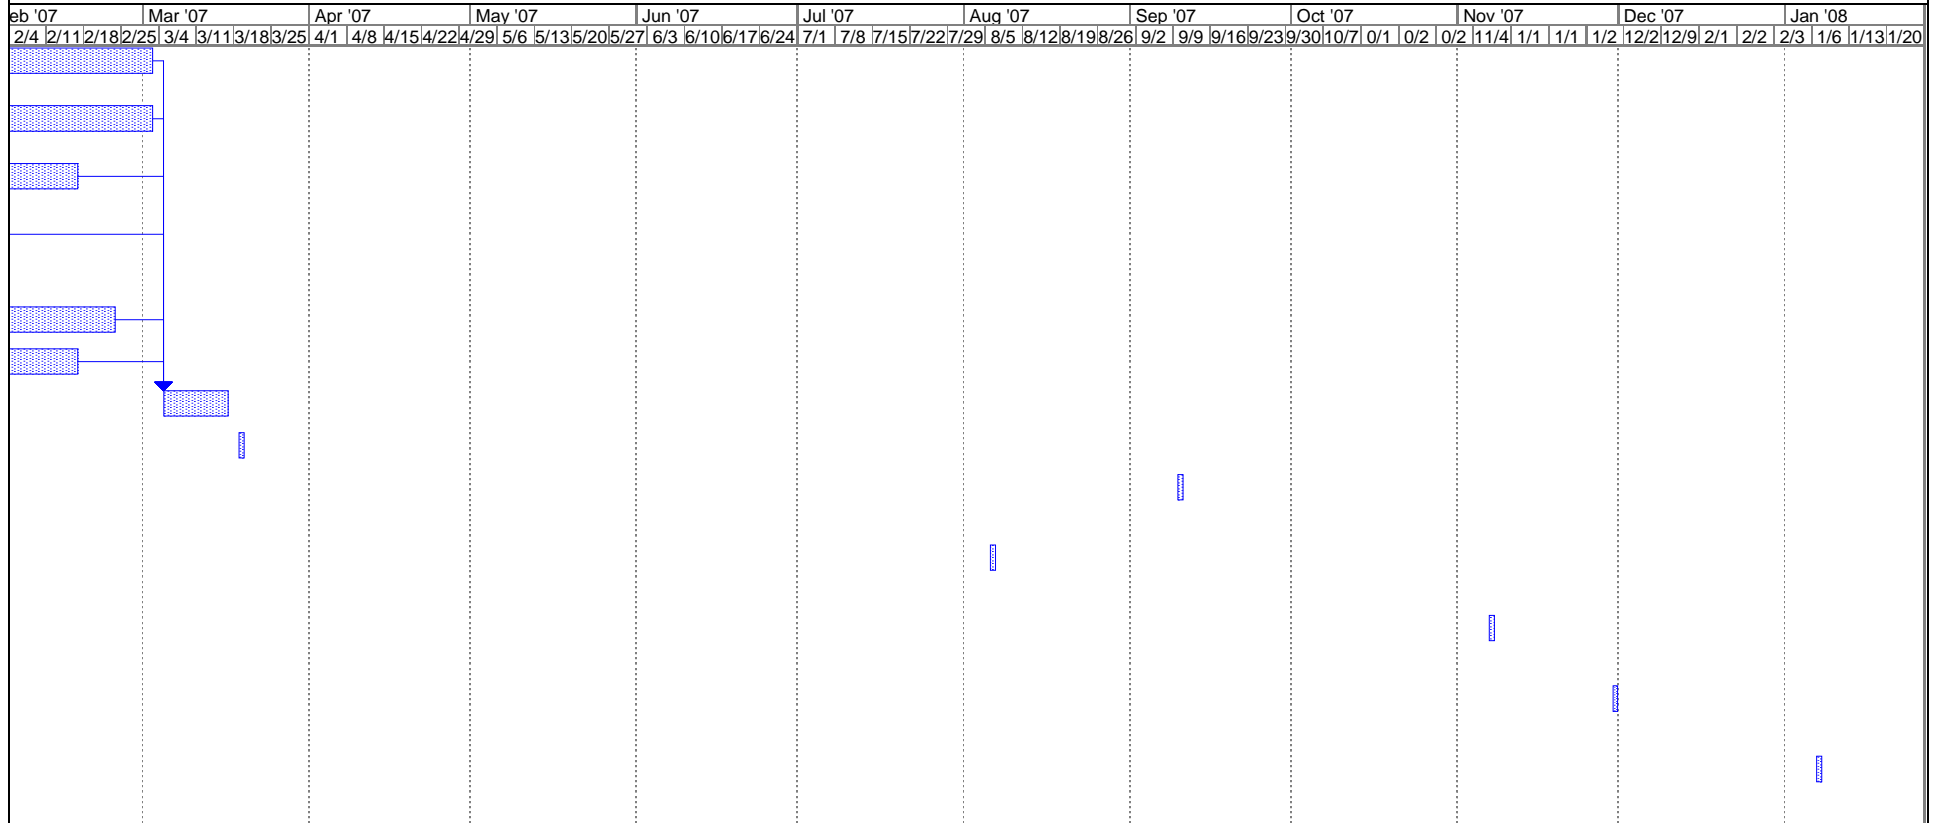


3rd row Headrest Mechanism
 Lisa Bilbrey
 January 16, 2007

Task		Summary		Rolled Up Progress		Project Summary	
Progress		Rolled Up Task		Split		Group By Summary	
Milestone		Rolled Up Milestone		External Tasks		Deadline	

Sequoia H/R Mech. ASY 71907-0C020 & 30 & 50



3rd row Headrest Mechanism
 Lisa Bilbrey
 January 16, 2007

Task		Summary		Rolled Up Progress		Project Summary	
Progress		Rolled Up Task		Split		Group By Summary	
Milestone		Rolled Up Milestone		External Tasks		Deadline	
